


Project Fact Sheet

Project Number	N/A
Project Title	SP - LED Streetlight Conversion
Project Manager	Nicole Allen

Project Information

City Wide Status




St Petersburg	
Total Lights to be Converted	30,376
Expected Completion Date	5/1/2021
Lights Completed to Date	2,701
Lights Remaining	27,675
On Target	

Zone Summary

Zone	Actual # of Install	Planned # of Installs	Remain # of Installs	Percent Complete
US/State Highway	733	773	40	95%
Zone 1	1968	5273	3305	37%
Zone 2	0	5658	5658	0%
Zone 3				
Zone 4				
Zone 5				
Zone 6				
Zone 7				

Overall Zone Map

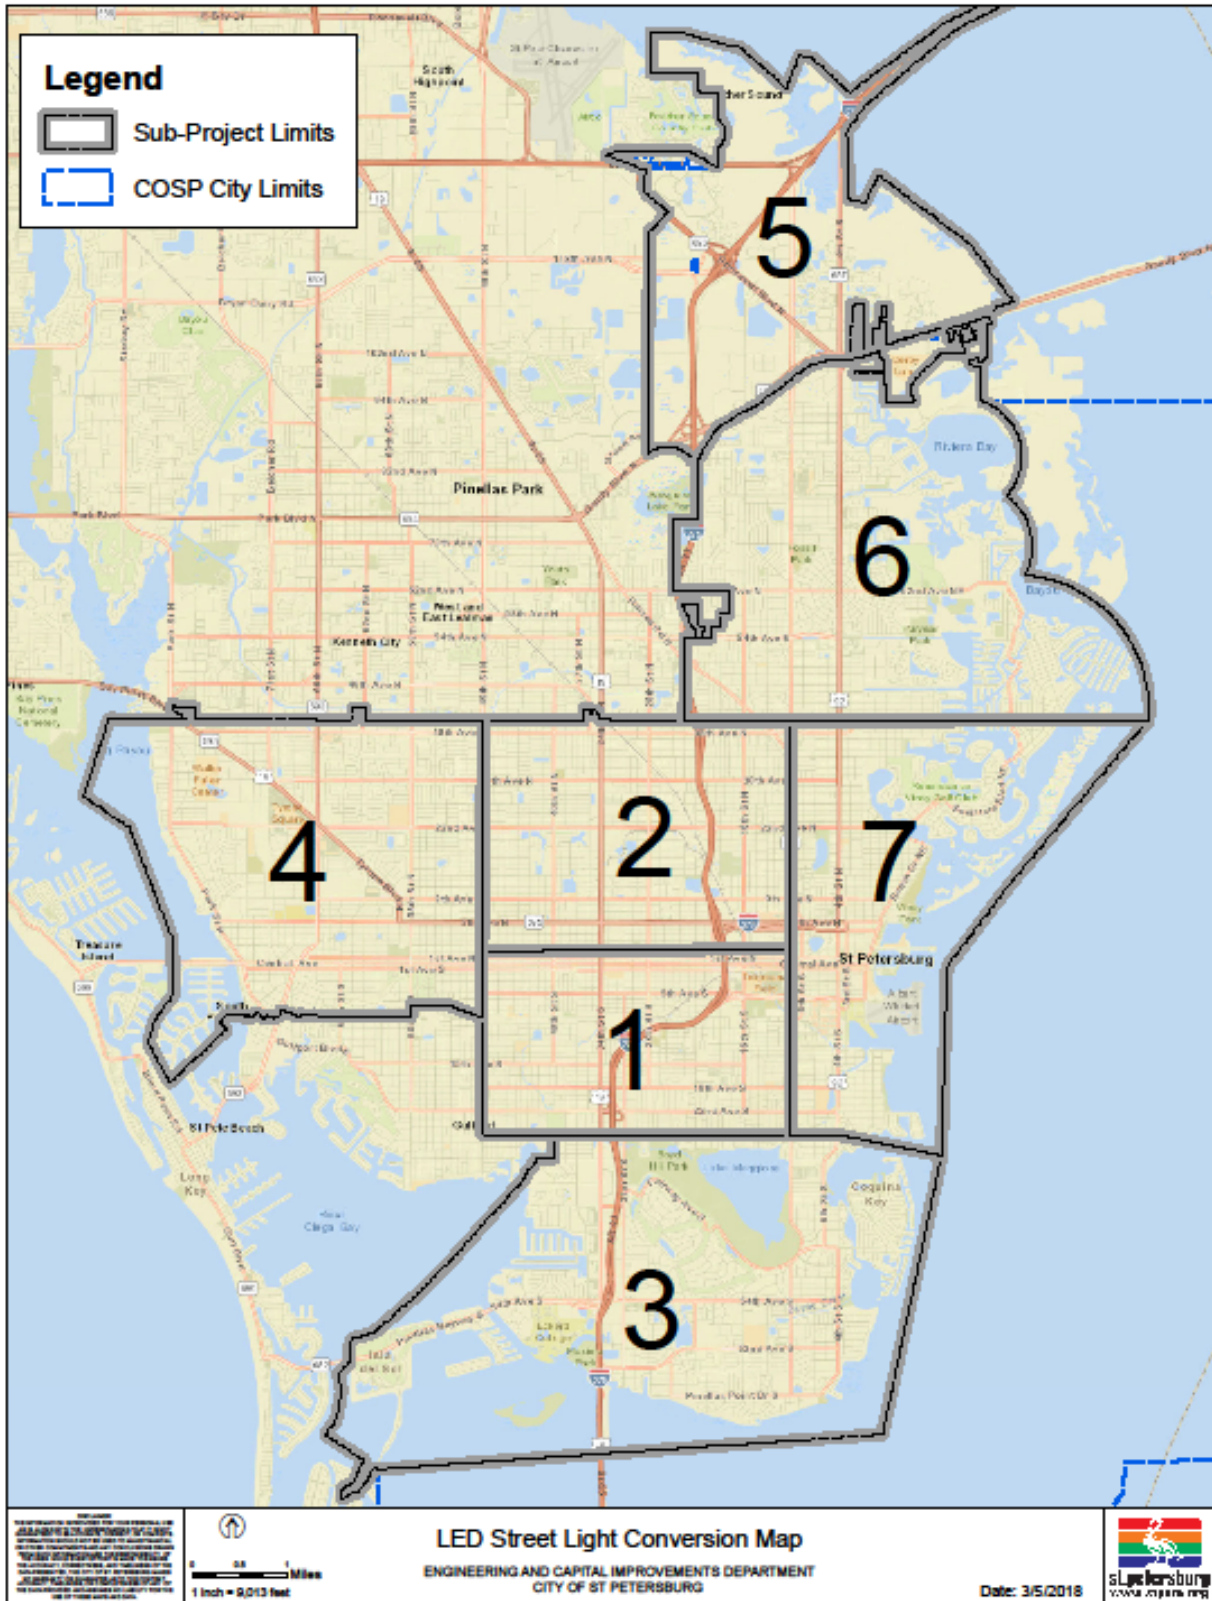

# Current Zone Map

